

SLICKLINE ASSISTANT WORKBOOK

IMPORTANT NOTE:

1. Your point of reference to complete this workbook may be obtained from the following
 - Training Manual and any other training materials provided together with this workbook
 - Your Trainer, Assessor (Slickline Operator), Verifier (FSM) or senior colleagues
 - SOP / Quality Procedures & Processors
2. The completion of this Workbook is a joint effort and responsibility between you and your assessor therefore you have the obligation to request from your assessor to be assessed upon your completion of each topic
3. The completion of this Workbook is part of the MANDATORY requirements which you must fulfill to qualify for a promotion
4. Your training program is mostly self-driven, including this Workbook. It requires individual initiatives, dedication and commitment to complete the process.

NAME	AMMAD SYAHIR BIN MOHAMMAD KHAIRUDDIN
DATE OF JOIN	9 March 2023
CONTACT NO.	01137454043
RECEIVED DATE	
DATE COMPLETED	



D. Rig up Wireline Surface Equipment

a. List out all surface equipment (Surface and Pressure Gauge)

1. Reel skid unit
2. Air compressor
3. Genset
4. Powerpack
5. Control panel
6. Telescopic mast
7. Inhibitor tank
8. Tool house
9. Test pump
10. Cabin
11. Lubricator skid
12. Sideline unit
13. Fugate unit

b. Describe how to connect lubricator section

i) Horizontal


put lubricator on stand and connect one by one

ii) Vertical

- connect lubricator using clamp and hanging using telescopic mark

Note: Provide drawing and parts description on separate paper/page

c. Sketch the equipment required while rigging up from x-mas tree until stuffing box

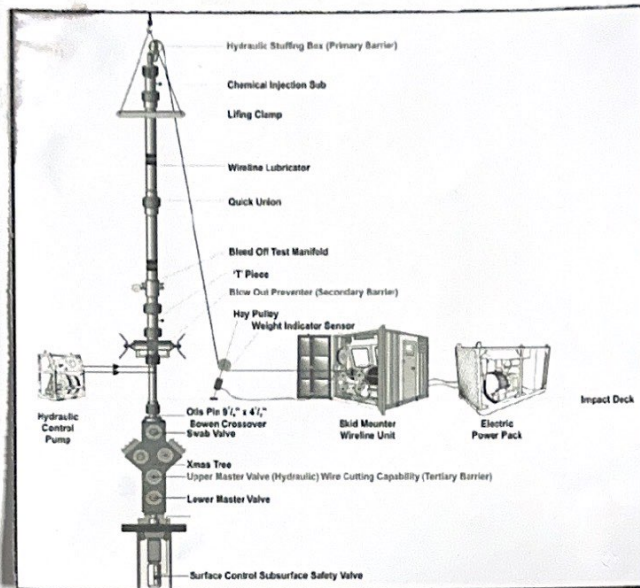

Note: Provide drawing and parts description on separate paper/page



d. What should weight indicator attached with?

- weight indicator attached with hose connect to load cell.

e. What is the meaning of rigging up and rigging down?

- rigging up is process assemble part equipment before start the work.
- rigging down is disassemble all part equipment upon the operation finish or shut well.

f. What is power pack hose size used at Dimension Bid?

- 1" for supply
- 1 1/2" for return

g. What are the safety precautions required upon completed hook up hydraulic hose to RSU

- connection need to be tighten
- use whipcheck for safety

h. List out the safety precaution while rigging up and rigging down

- Full PPE
- use proper handtool during lifting part
- Barricade work area
- TBT with crew

Note: Provide drawing and parts description on separate paper/page



DIMENSION BID

WELL INTERVENTION | PERFORATION SERVICES

Document No: DBSB-SLS-09
Revision No.: 00
Revision Date: 01/10/2018

CONTROLLED COPY
