



**D. Rig up Wireline Surface Equipment**

a. List out all surface equipment (Surface and Pressure Gauge)

- |                                       |
|---------------------------------------|
| 1. Generator                          |
| 2. Air Compressor                     |
| 3. Power Pack                         |
| 4. Reel skid unit PSU (wireline wind) |
| 5. Stuffing Box                       |
| 6. Hydraulic mast                     |
| 7. Lubricator                         |
| 8. Cross over                         |
| 9. Blow out Preventer (BOP)           |
| 10. Quick Test Sub (QTS)              |
| 11. Ball valve                        |
| 12. Control Panel (CP, SWCP, WCP)     |
| 13. Hay Ralley                        |

b. Describe how to connect lubricator section

i) Horizontal

- Lay down using trolley and stand using sling/rope & connect lubricator to either PCE.

ii) Vertical


- Align the pin to box properly to avoid damaging the O-ring.

*(Signature)*  
**GAZALI MEHRY**  
Operation Manager  
Dimension Bid (M) Sdn Bhd  
(East Malaysia Operation)

30/11/22

*Note: Provide drawing and parts description on separate paper/page*

c. Sketch the equipment required while rigging up from x-mas tree until stuffing box

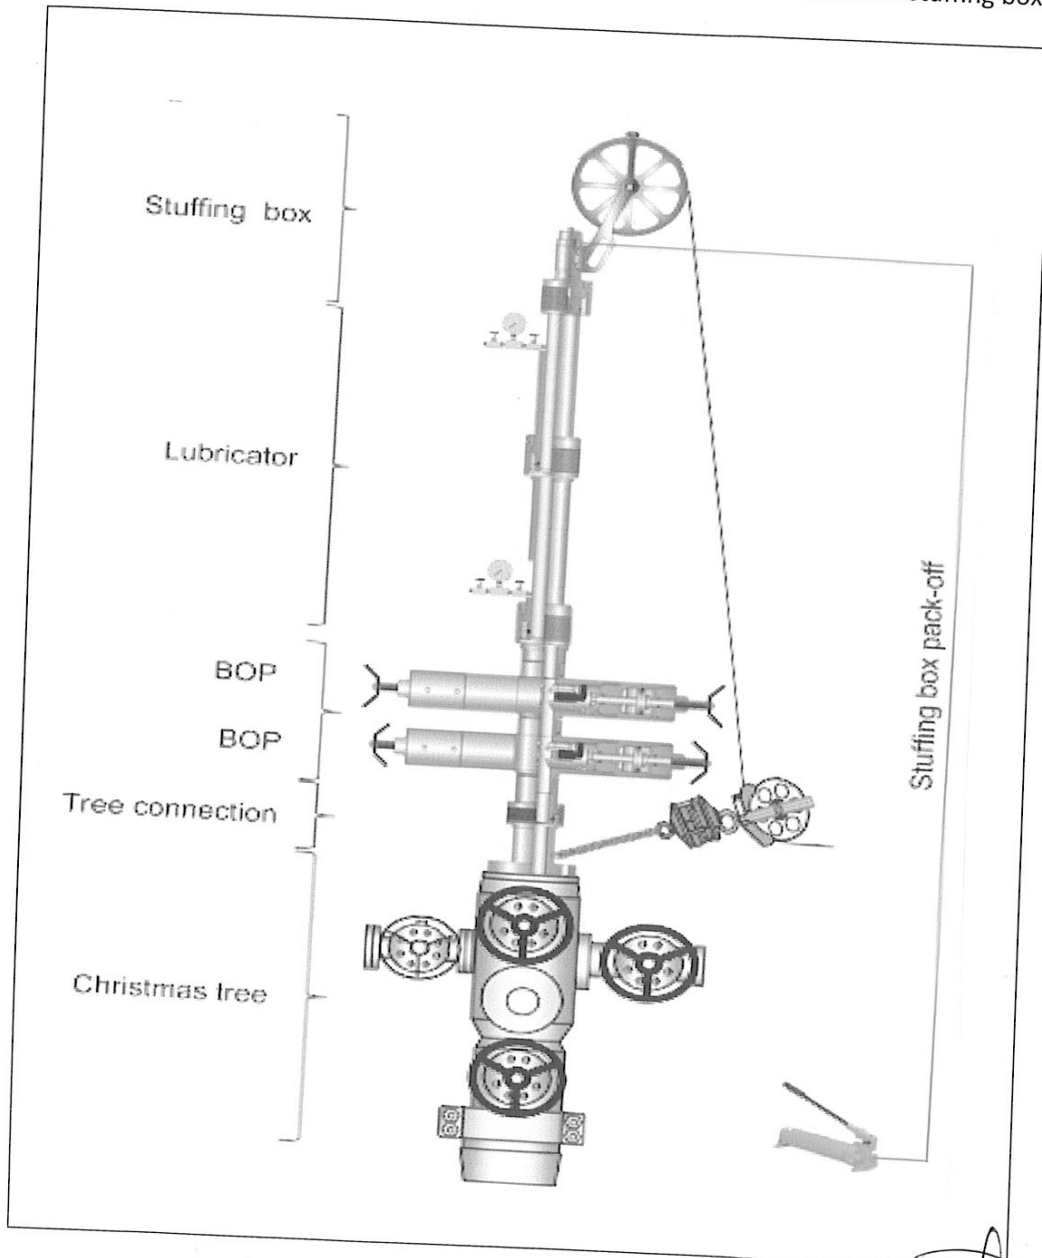

*Note: Provide drawing and parts description on separate paper/page*

GAZALI MEHRY  
Operation Manager  
Dimension Bid (M) Sdn Bhd  
(East Malaysia Operation)

30/11/22



d. What should weight indicator attached with?

- Load Cell
- Hay Pulley

e. What is the meaning of rigging up and rigging down?

- Rig up: Prepare equipment for operation.
- Rig down: Disassemble equipment to ready for demob/move to another location.

f. What is power pack hose size used at Dimension Bid?

- 1" : Supply
- 1 1/2" : Return

g. What are the safety precautions required upon completed hook up hydraulic hose to RSU

- make sure the connection is properly connected.
- make sure there is no leakage.
- make sure the lock ring is in place.

h. List out the safety precaution while rigging up and rigging down

- Full PPE
- Following the procedure/instruction
- Tool box meeting before operation.

Note: Provide drawing and parts description on separate paper/page

**GAZALI MEHRY**  
Operation Manager  
Dimension Bid (M) Sdn Bhd  
(East Malaysia Operation)

30/11/22
