

D. Rig up Wireline Surface Equipment

a/ List out all surface equipment (Surface and Pressure Gauge)

✓ 1. Reel skid Unit.
✓ 2. Air Compressor.
✓ 3. genset.
✓ 4. Power Pack.
✓ 5. Control panel.
✓ 6. Telescopic Mast.
✓ 7. Intisifier Tank.
✓ 8. Tool House
✓ 9. Tool Box
✓ 10. Cabin
✓ 11. Lubriator skid.
✓ 12. Slimline Unit
✓ 13. Plyline Unit.

b. Describe how to connect lubricator section


i) Horizontal
 ✓ - Put lubricator on stand and connect one by one.

ii) Vertical
 ✓ - Connect lubricator using clamp and hanging using telescopic mast.

Handwritten signature
 19/01/23

Note: Provide drawing and parts description on separate paper/page

c. Sketch the equipment required while rigging up from x-mas tree until stuffing box

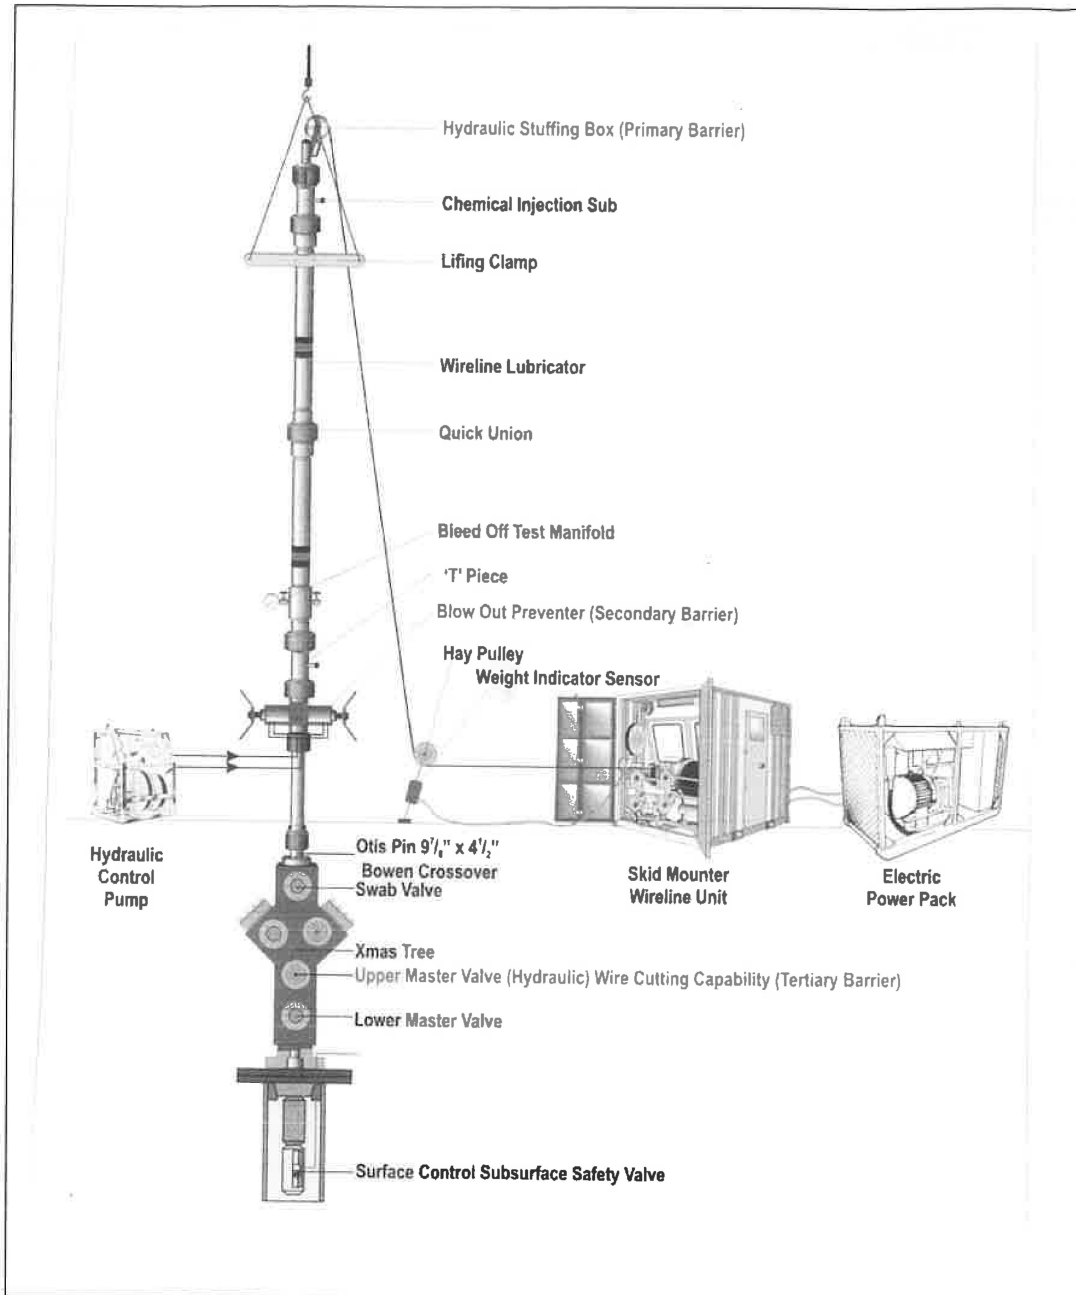

Note: Provide drawing and parts description on separate paper/page

*Not
1/6/23*



d. What should weight indicator attached with?

✓ Weight indicator attached with hose & connected to load cell.

e. What is the meaning of rigging up and rigging down?

✓ Rig up is process assemble part equipment before start the work.
✓ Rig down is disassemble all part equipment when the operation finish or skid well.

f. What is power pack hose size used at Dimension Bid?

✓ 1" supply
✓ 1 1/4" return.

g. What are the safety precautions required upon completed hook up hydraulic hose to RSU

✓ Connection need to be tighten.
✓ Use whip check for safety.
✓ Safety pin.

h. List out the safety precaution while rigging up and rigging down

✓ Full PPE.
✓ Use proper hand tool during handling part.
✓ Barricade work area.
✓ TBT with crew.

Note: Provide drawing and parts description on separate paper/page

Handwritten signature and date: 12/6/23

