

15/01/2024 (Monday)

SEAH #3 PACKAGE



Skid

- Chipping all the rust on skid body using chipping tool machine

when using chipping tool machine, we must protect our ears using ear plug or ear muffs.

Hearing protectors are required to prevent noise induced hearing loss. Hearing protection devices reduce the noise energy reaching and causing damage to the inner ear. Ear muffs and earplugs are the most common types of PPE.

- Repaint the skid with green paint

16/01/2024 (Tuesday)

Preparation for SEAH #3 package



- Put lubricator inside skid
- Repaint Dolley trolley stand
- Put other PCE configuration inside open tray

Inside open tray



- PTU
- SWCP
- Pup joint
- Pump in tee
- Bop hose
- Air hose
- Stuffing box hose
- Quick test sub hose
- SWCP hose

17/01/2024 (Wednesday)

Final preparation for SEAH #3 package



- Learn how to tie tagline and install it on skid and open tray and WCP



- Install sling and shackle
- Install safety pin on shackle


The shackle is secured using a nut and bolt, with the safety pin providing an extra layer of fastening to further safeguard against the shackle coming loose



- Put wire rope lube on sling to prevent sling from damage

18/01/2024 (Thursday)

Assist SE team

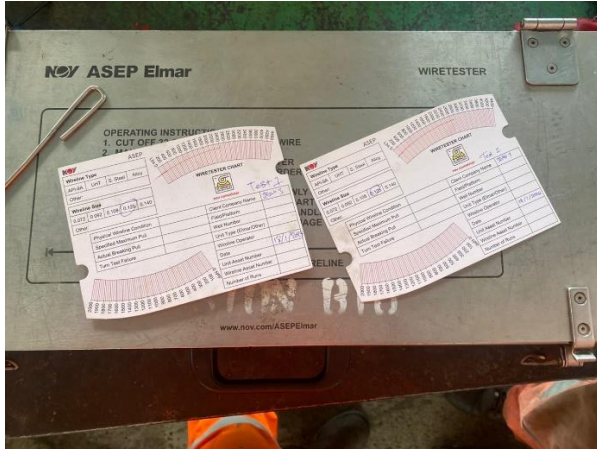

- Assist and learn how to test maximum wire tension using wire tester.
- The wire size that we use is 0.125.

Wireline Type	API-9A	UHT	S. Steel	Alloy	
Other:					
Wireline Size	0.072	0.092	0.108	0.125	0.140
Other:					
Physical Wireline Condition		Client Company Name	SEAH 3		
Specified Maximum Pull		Field/Platform			
Actual Breaking Pull		Well Number			
Turn Test Failure		Unit Type (Elmar/Other)			
		Wireline Operator			
		Date	18/1/2024		
		Unit Asset Number			
		Wireline Asset Number			
		Number of Runs			

Wireline Type	API-9A	UHT	S. Steel	Alloy	
Other:					
Wireline Size	0.072	0.092	0.108	0.125	0.140
Other:					
Physical Wireline Condition		Client Company Name	SEAH 3		
Specified Maximum Pull		Field/Platform			
Actual Breaking Pull		Well Number			
Turn Test Failure		Unit Type (Elmar/Other)			
		Wireline Operator			
		Date	18/1/2024		
		Unit Asset Number			
		Wireline Asset Number			
		Number of Runs			

Wireline Type	API-9A	UHT	S. Steel	Alloy	
Other:					
Wireline Size	0.072	0.092	0.108	0.125	0.140
Other:					
Physical Wireline Condition		Client Company Name	SEAH 3		
Specified Maximum Pull		Field/Platform			
Actual Breaking Pull		Well Number			
Turn Test Failure		Unit Type (Elmar/Other)			
		Wireline Operator			
		Date	18/01/24		
		Unit Asset Number			
		Wireline Asset Number			
		Number of Runs			

- We did 3 tests for the wire
- The result is 2500 lbs (test 1), 2700 lbs (test 2), 2700 lbs (test 3).

Prepare second WCP for ROC drilling package.



- Chipping all the rust using chipping tool machine
- Apply primer paint (red)



- Took off all the gauges to send to calibration
- Before took off all the gauges, it is a must to bleed all the pressure inside the WCP to prevent blow out from the gauges.

19/01/2024 (Friday)

Continue prepare second WCP for ROC drilling package.



- Wash WCP using degreaser and rinse out it with water



- Repaint WCP using green paint to make it look new.

DIMENSION BID

Slickline Assistant Onshore On-the-Job Training Record


Trainee's Name:	MUHAMMAD AHSAN BIN ZAINUDDIN	Job Title:	TRAINEE SLICKLINE ASSISTANT
Month:	JANUARY	Training Period:	15/01/2024 - 19/01/2024

No.	Main Tasks (please describe tasks and specify name of tools / equipment)	Training Date	Training Time		Total Hours	PR*	Signature	
			From	To			Trainee	Instructor
1	SKID (SEAT 3) - Chipping and repaint skid	15/01/2024 (MONDAY)	0800	1700	8	S		
2	Preparation for SEAT 2 package - put lubricator inside skid - repaint Dolly tray stand - put other ref configuration inside open tray	16/01/2024 (TUESDAY)	0800	1700	8	S		
3	Final preparation for SEAT 2 package - install trackline - install sling and shackle - install safety pin - put wire rope lube on sling to prevent damage	17/01/2024 (WEDNESDAY)	0800	1700	8	S		
4	Assist SE team - assist and learn how to test ^{maximum} wire tension using wire tester. Roe driving WEP - chipping all the rust and apply primer paint - took off all the gauges to saddle to calibration.	18/01/2024 (THURSDAY)	0800	1700	8	S		
5	WEP for Roe driving package - wash with degreaser and hose it out using water - Repaint WEP with green paint to make it look new.	19/01/2024 (FRIDAY)	0800	1700	7	S		

Total Hours 29

* Performance Rating (PR): S - Strong A - Adequate N - Improvement Needed

DIMENSION BID

Approved by:		Overall Assessment:
Designation	LEONARD RAEYONG Maintenance Manager	
Date	Dimension Bid (M) Sdn Bhd Labuan Warehouse Slickline Services	

2 5
2 5
2 5
2 5
2 5
