




SLICKLINE ASSISTANT WORKBOOK

IMPORTANT NOTE:

1. Your point of reference to complete this workbook may be obtained from the following
 - Training Manual and any other training materials provided together with this workbook
 - Your Trainer, Assessor (Slickline Operator), Verifier (FSM) or senior colleagues
 - SOP / Quality Procedures & Processors
2. The completion of this Workbook is a joint effort and responsibility between you and your assessor therefore you have the obligation to request from your assessor to be assessed upon your completion of each topic
3. The completion of this Workbook is part of the MANDATORY requirements which you must fulfill to qualify for a promotion
4. Your training program is mostly self-driven, including this Workbook. It requires individual initiatives, dedication and commitment to complete the process.

NAME	SELVESTER SILO ANAK KELLY
DATE OF JOIN	02.09.2024
CONTACT NO.	01117594205
RECEIVED DATE	05.02.2025
DATE COMPLETED	25.02.2025


GAZALI MENNI
Operation Manager
Dimension Bid (M) Sdn Bhd
Labuan Warehouse
Slickline Services

26/2/25

D. Rig up Wireline Surface Equipment


a. List out all surface equipment (Surface and Pressure Gauge)

1. Generator Set
2. Air compressor
3. Powerpack
4. Reel Skid Unit (RSU)
5. Stuffing Box
6. Wireline Mast
7. Lubricator
8. Crossover
9. Blow Out Preventor (BOP)
10. Quick Test Sub (QTS)
11. Ball Valve
12. Hay Pulley
13. Single Well Control Panel (SWCP)

b. Describe how to connect lubricator section

i) Horizontal

Lay down the lubricator on the dolly trolley and connect three 8ft lubricator sections to the stuffing box at the top. Attach a lifting clamp to the top section of the lubricator. Assemble the necessary equipment for both above and below the BOP, based on the wireline work to be performed. Ensure all quick unions are make-up hand tight.


GAZALI MEHRY
 Operation Manager
 Dimension Bid (M) Sdn Bhd
 Labuan Warehouse
 Slickline Services
 26/2/25

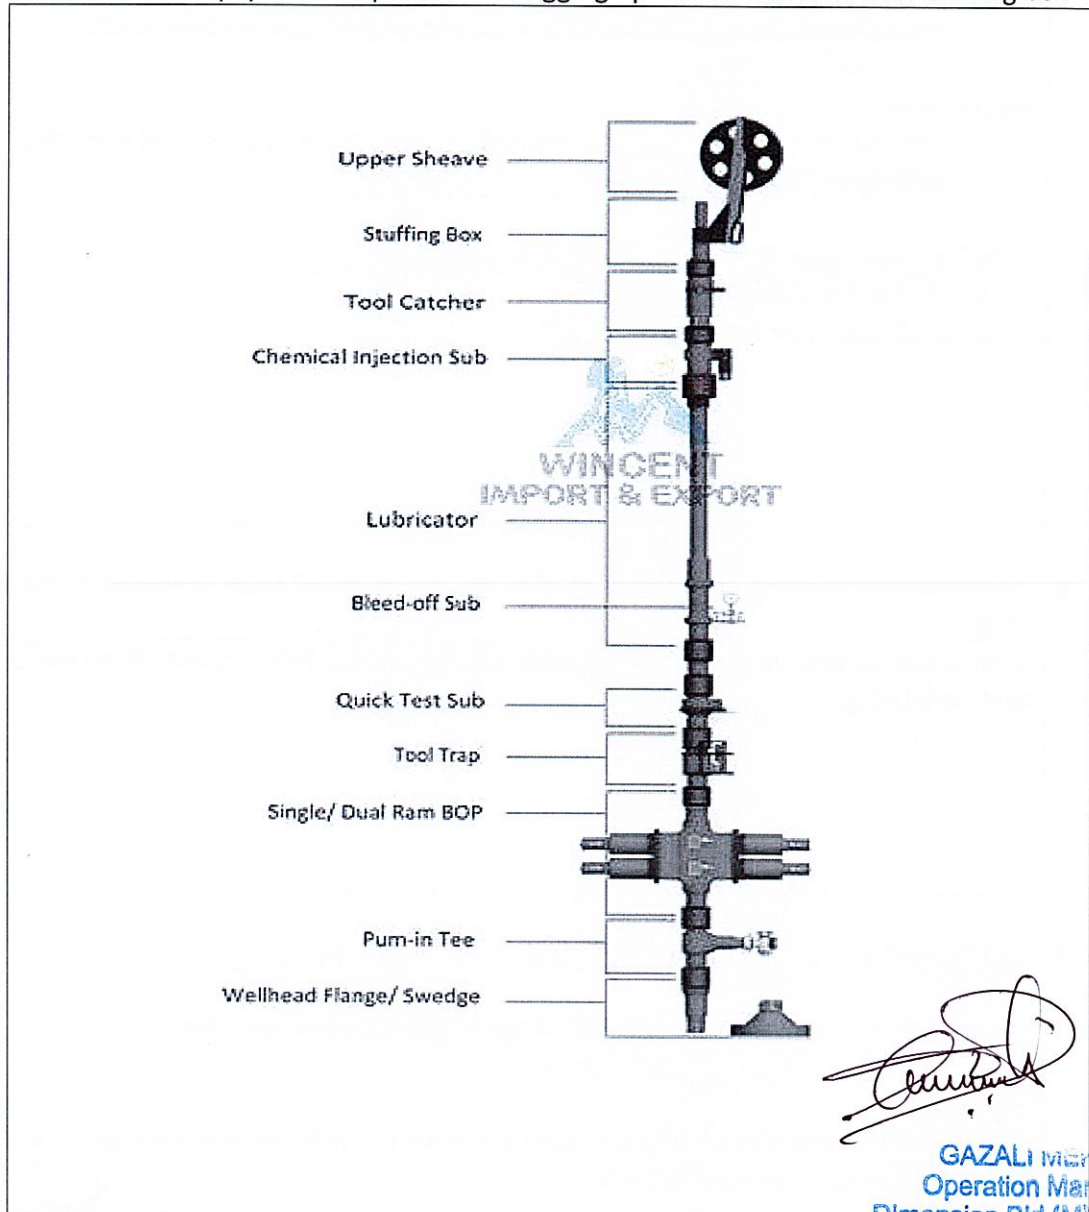


ii) Vertical

Install the lubricator riser or adaptor to the tree cap connection, whichever is applicable. The wireline assistant on the wireline deck shall tie the chain block onto the other end of the length of rope held by the assistant on the gin pole. Secure lifting hook of the chain block to the lubricator lifting clamp. Hoist the lubricator by pulling the chain on the chain block until the lubricator is picked up to the required height for stabbing onto the Xmas tree or adaptor.

Note: Provide drawing and parts description on separate paper/page

c. Sketch the equipment required while rigging up from x-mas tree until stuffing box



Note: Provide drawing and parts description on separate paper/page

GAZALI MERRY
Operation Manager
Dimension Bid (M) Sdn Bhd
Labuan Warehouse
Slicking Services

26/2/25



d. What should weight indicator attached with?

Load Cell and Hay Pulley.

e. What is the meaning of rigging up and rigging down?

Rigging Up

- The process of assembling and setting up all necessary equipment, tools, and machinery for a specific operation, such as preparing the rig for a job.

Rigging Down

- The process of disassembling, removing, and securing equipment after the operation is completed.

f. What is power pack hose size used at Dimension Bid?

- 1" hose size for supply.
- 1 ½" hose size for return.

g. What are the safety precautions required upon completed hook up hydraulic hose to RSU

Ensure that all hose is connected properly and lock ring is lock in place. Then make sure no leaking.

h. List out the safety precaution while rigging up and rigging down

Rig Up

- Secure Loose Items, Wear PPE, Proper Lifting Techniques, Clear Communication, Check Connections

Rig Down

- Depressurized Equipment, Proper Handling of Tools, Secure Equipment, Wear PPE, Proper Lifting Method

Note: Provide drawing and parts description on separate paper/page

26/2/25
